


Project-space model for ABC Enterprises Finance Upgrade


As at: 30.04.2021

Project contact: Brittany Sparks

Project-space - forecast:

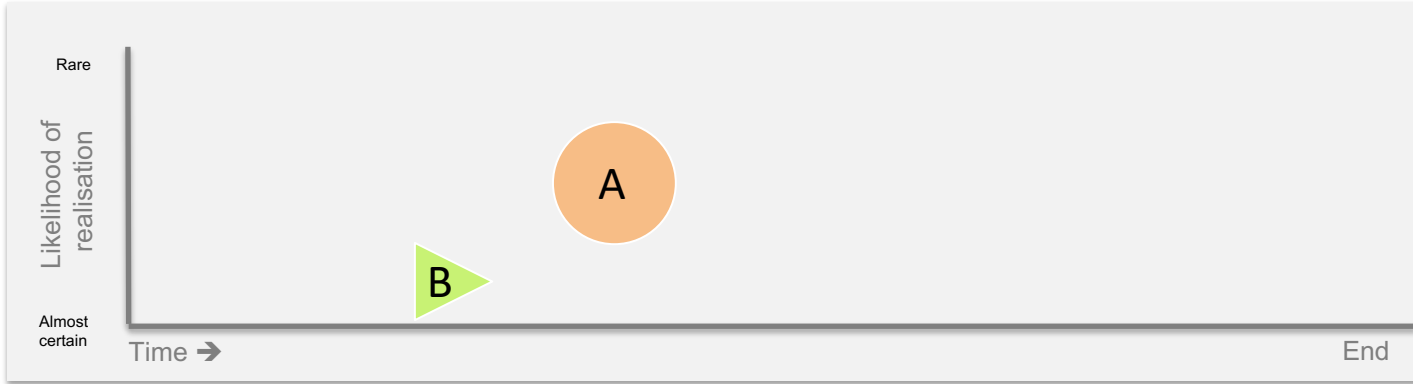

Project-space - current:

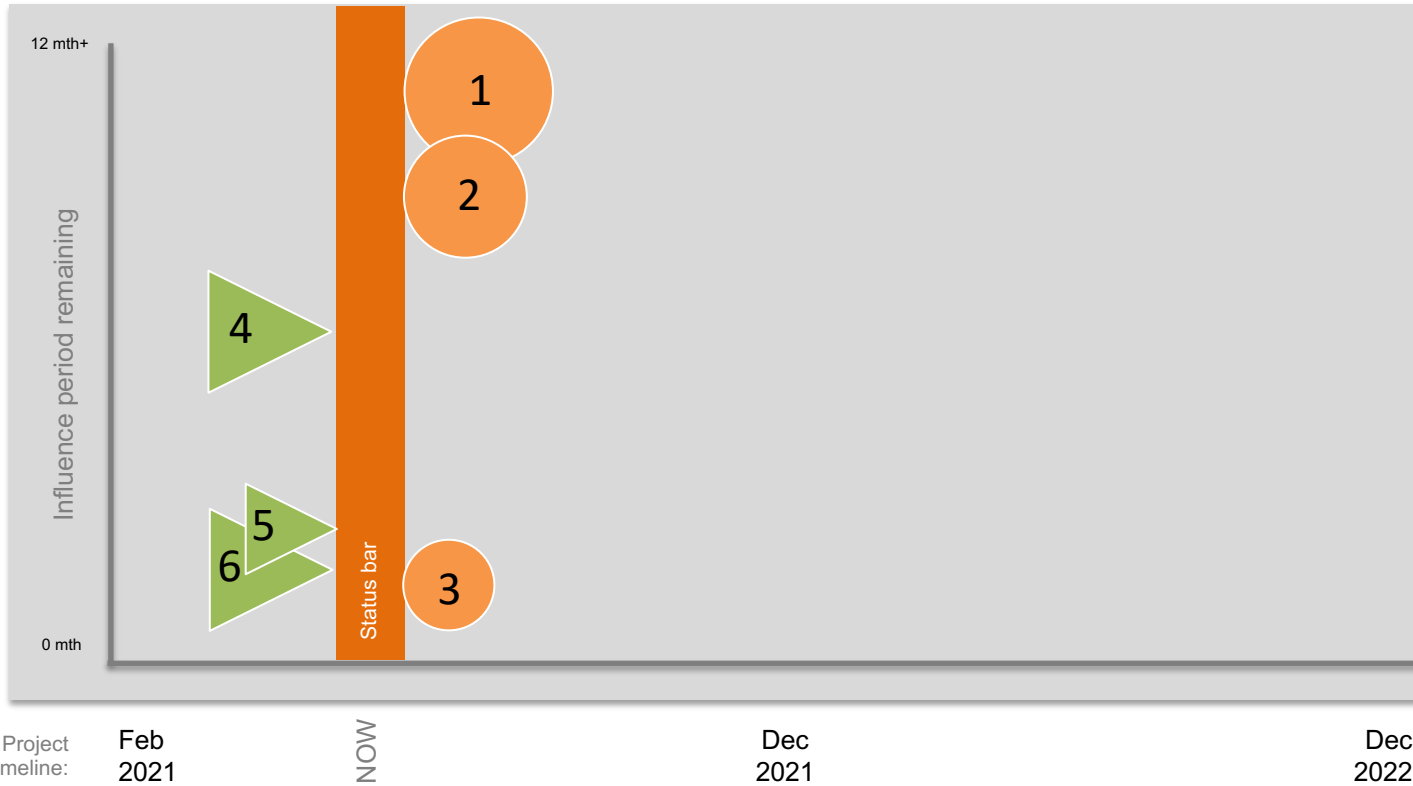

Legend

- 1: IT cannot provide required information to inform requirements gathering. [Ranking = 4]
 - 2: Project team lack project experience this impacts the efficiency of the initiatives management. [Ranking = 3]
 - 3: Delays in analysts completion of requirements development. [Ranking = 2]
 - 4: Project board is influential and can drive progress and resolve problems. [Ranking = 3]
 - 5: Business Analysts skilled in requirements gathering. [Ranking = 2]
 - 6: Finance staff support for the initiative. [Ranking = 3]
- A:** There is a threat that the payroll system may change resulting in different integration requirements. [Ranking = 3]
- B:** There is an opportunity for the project support officer to upskill and become more efficient. [Ranking = 1]

- Enabler *Larger shapes have greater impact/potential impact.*
- Constraint *Smaller shapes have lesser impact/potential impact.*
- Opportunity
- Threat

Ranking 1 = least impact
Ranking 5 = most impact


New to PSM

Project-space model for Blackiron Country EDRMS Project


As at: 30.06.2017

Project contact: Janine Smith

Project-space - forecast:

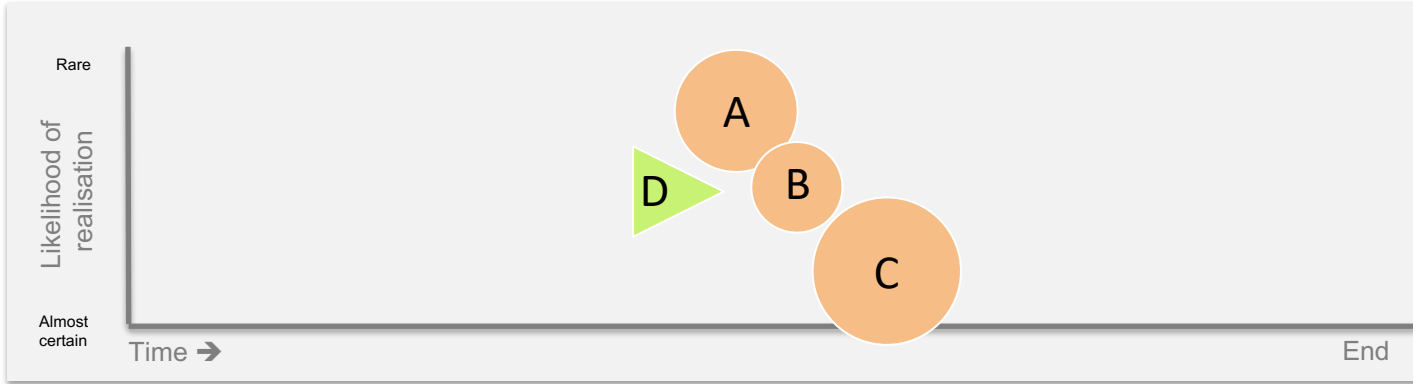

Project-space - current:

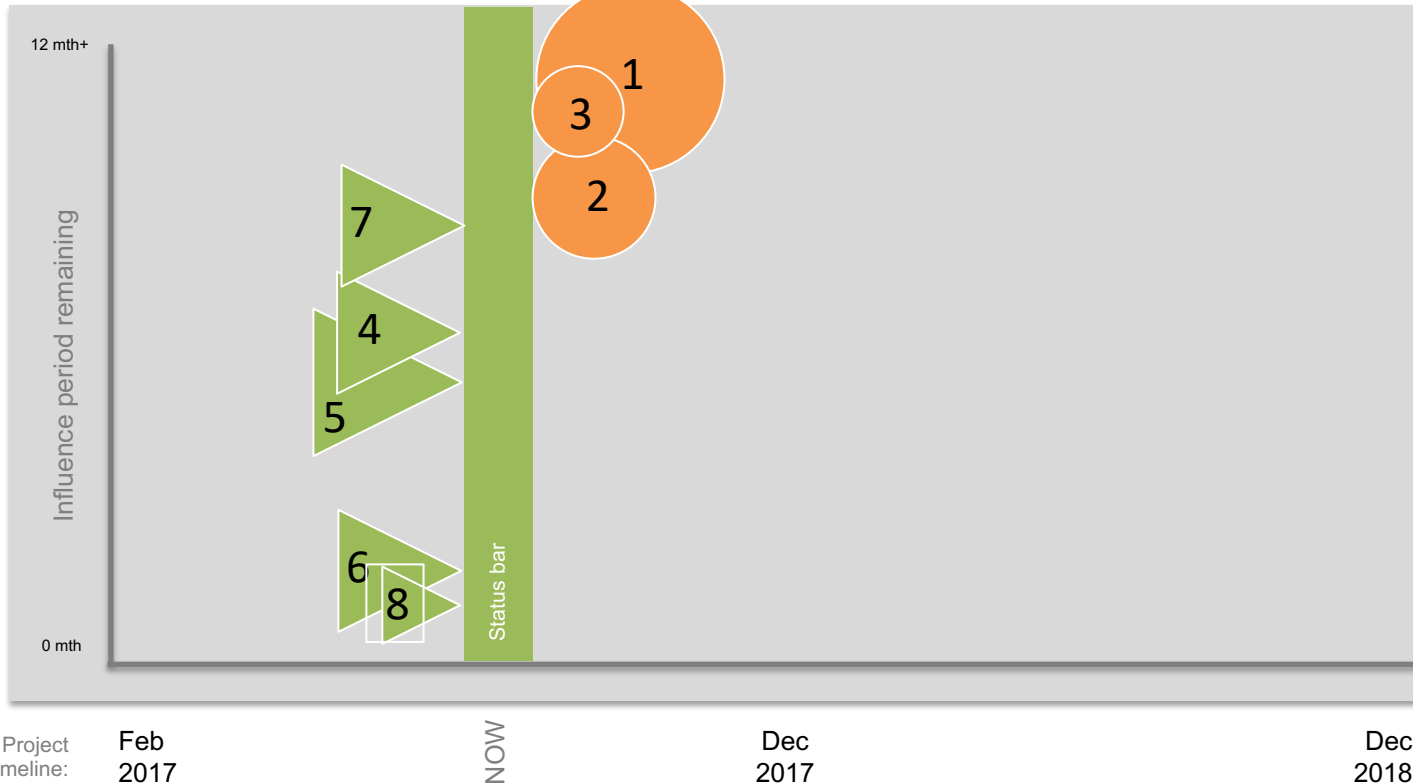

Legend

1: Project Board have not signed off on requirements specification, preventing commencement of system design and build. [Ranking = 5]

2: Project team do not have PRINCE2/project experience this impacts the efficiency of the initiatives management. [Ranking = 3]

3: Mild resistance to the transition to EDRMS from nursing and records staff. [Ranking = 2]

4: Authoritative and influential board that can drive progress and resolve problems. [Ranking = 3]

5: System requirements have been finalised. [Ranking = 4]

6: Medical staff support for the initiative. [Ranking = 3]

7: Funding for implementation and training has been released. [Ranking = 3]





8: Project Support Officer's skills are enabling project efficiencies.. [Ranking = 1]

A: There is a threat that the patient billing system may change resulting in different integration requirements. [Ranking = 3]

B: There is a threat that there will be new system security requirements that need to be incorporated into the system's design. [Ranking = 2]

C: There is a threat of strong resistance from nursing and medical staff that may impact the realisation of the EDRMS implementation. [Ranking = 4]

D: There is an opportunity for an increase in the number of staff who are available to support change management activities due to a record's clerk potentially having spare capacity. [Ranking = 2]

-  **Enabler** *Larger shapes have greater impact/potential impact.*
-  **Constraint**
-  **Opportunity** *Smaller shapes have lesser impact/potential impact.*
-  **Threat**

Ranking 1 = least impact
Ranking 5 = most impact

 **New to PSM**

Icon Set

Just take copies of these- so you can use each shape more than once

Impact/
potential
impact





Opportunities

Threats

Enablers

Constraints

5







Within Org's Control




Outside Org's Control






4







3







Last Month's size



2



1



More significant
(larger)

Less significant
(smaller)

